

# 23<sup>rd</sup> Street, Columbus

## Weekly Public Relations Report

### Date

May 13, 2025

### Work from Last Week

- Water Main: Install water main from west of 26<sup>th</sup> Ave to 28<sup>th</sup> Ave.
- Storm Sewer: Install storm sewer from east of 23<sup>rd</sup> Ave to 24<sup>th</sup> Ave.
- Removals: Remove existing pavement from 28<sup>th</sup> Ave to 31<sup>st</sup> Ave.

### Work Anticipated This Week

- Water Main: Install water main from 27<sup>th</sup> Ave to west of 28<sup>th</sup> Ave.
- Storm Sewer: Install storm sewer trunkline from east of 24<sup>th</sup> Ave to 26<sup>th</sup> Ave. Build inlets and manholes from 23<sup>rd</sup> Ave to 26<sup>th</sup> Ave.

### Work Anticipated Next Week


- Water Main: Install water main from west of 28<sup>th</sup> Ave to west of 30<sup>th</sup> Ave.
- Storm Sewer: Install storm sewer trunkline from 26<sup>th</sup> Ave to 28<sup>th</sup> Ave. Build inlets and manholes from 25<sup>th</sup> Ave to 27<sup>th</sup> Ave.

### Next Major Milestone(s)

- Open newly constructed eastbound lanes to traffic, tentatively scheduled for early fall 2025.

# COLUMBUS 23RD STREET MONTHLY PROGRESS REPORT

## APRIL 2025

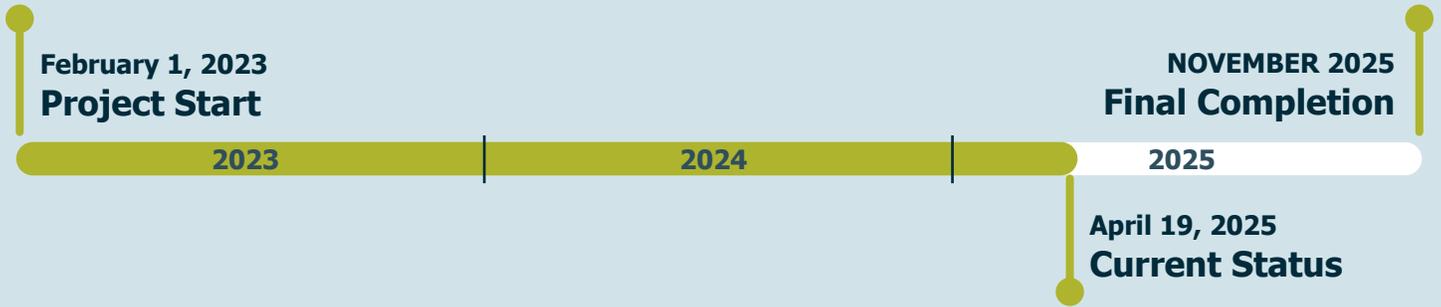

### April 2025 Construction Update

**Work That Occurred This Month:** In April 2025, construction resumed on the last major phase of the project. This phase will be reconstruction of 23rd St from just west of 18th Ave to 31st Ave in the eastbound lanes. Work this month consisted of pavement removals from 18th Ave to near 28th Ave, new water main from 18th Ave to 26th Ave, and new storm sewer from 18th Ave to Pershing Rd.

**Work That Has Occured to Date:** This project began in late summer 2022 with remediation of an EPA superfund site just east of 26th Ave. Work commenced on the core scope of the project in 2023 with reconstruction of eastbound and westbound lanes from west of 14th Ave to east of East 11th Ave including storm sewer, water main, sanitary sewer, roadway lighting, and traffic signal upgrades. Work resumed in 2024 with reconstruction of the westbound lanes from 31st Ave to west of 14th Ave as well as the eastbound lanes from west of 18th Ave to west of 14th Ave. This stretch also consisted of new concrete pavement, as well as storm sewer, water main, roadway lighting, and traffic signal upgrades.



## PROJECT HIGHLIGHTS



Percentage of the total monetary contract completed to date.




Percentage of total concrete pavement placed, including highway pavement, driveways, intersections, and sidewalks. Also included, but not limited to, incidental work such as stabilized subgrade, crushed concrete base course, etc.



Percentage of electrical work completed, including signalization and lighting.




Percentage of storm sewer work completed, including sewer pipe, manholes, curb inlets, and area inlets.



Percentage of new water main work completed, including water main services and crossings.



# COLUMBUS 23RD STREET CONSTRUCTION SCHEDULE

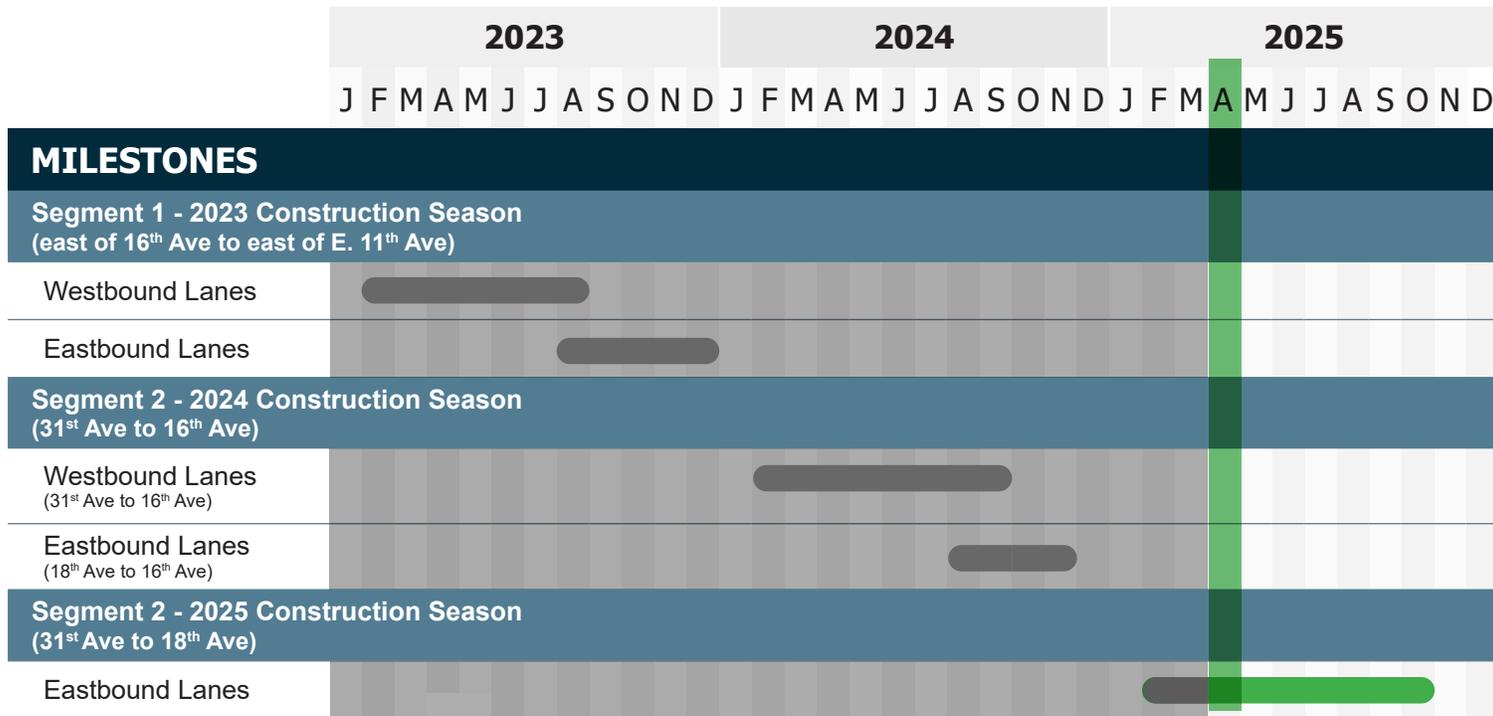

**Phase Legend (horizontal lines):**

- █ On or ahead of schedule
- █ Less than or equal to 1 month behind schedule
- █ More than 1 month behind
- █ Complete

**Project Progress Bar Legend (vertical line):**

- █ On or ahead of schedule
- █ Less than or equal to 1 month behind schedule
- █ More than 1 month behind schedule

**All traffic changes are weather dependent.**

Visit [ndot.info/32234](http://ndot.info/32234) or scan the QR code for more information.



# COLUMBUS 23RD STREET MONTHLY PROGRESS REPORT | APRIL 2025

**2025**

**EASTBOUND:**

31<sup>st</sup> Ave - 23<sup>rd</sup> Ave  
(Spring - Summer)

23<sup>rd</sup> Ave - 18<sup>th</sup> Ave  
(Spring - Summer)

