















































































ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Actual Start	Actual Finish
1			Summer Work '26	75 days?	Mon 5/4/26	Fri 8/14/26		Mon 5/4/26	NA
2			Dismissal for Summer	1 day	Tue 5/19/26	Tue 5/19/26		Tue 5/19/26	Tue 5/19/26
3			Rennovation	61 days?	Mon 5/4/26	Mon 7/27/26		NA	NA
4			Shop area	39 days	Mon 5/4/26	Thu 6/25/26		NA	NA
5			MEP Demo	3 days	Mon 5/4/26	Wed 5/6/26		NA	NA
6			Cederburg Demo	10 days	Thu 5/7/26	Wed 5/20/26	5	NA	NA
7			Install lintles and soap in beams	3 days	Thu 5/21/26	Mon 5/25/26	6	NA	NA
8			CMU walls (rm 172S,171S,163)	3 days	Thu 5/21/26	Mon 5/25/26	6	NA	NA
9			Below grade rough in	2 days	Thu 5/21/26	Fri 5/22/26	6	NA	NA
10			Foundation (CF-5,CF-1,	2 days	Thu 5/21/26	Fri 5/22/26	6	NA	NA
11			Install stairs on east side	1 day	Tue 5/26/26	Tue 5/26/26	7	NA	NA
12			CMU Walls (remaining)	3 days	Tue 5/26/26	Thu 5/28/26	8,10	NA	NA
13			Slab and ramp pour	2 days	Fri 5/29/26	Mon 6/1/26	12	NA	NA
14			Install overhead door	1 day	Tue 6/2/26	Tue 6/2/26	13	NA	NA
15			Install lights	2 days	Tue 6/2/26	Wed 6/3/26	13	NA	NA
16			Fire sprinklers	5 days	Tue 6/2/26	Mon 6/8/26	13	NA	NA
17			Tooth and infill	2 days	Fri 5/29/26	Mon 6/1/26	12	NA	NA
18			Drywall (concession 18	1 day	Thu 5/21/26	Thu 5/21/26	6	NA	NA
19			Wall rough (All MEP)	2 days	Fri 5/22/26	Mon 5/25/26	18	NA	NA
20			Install Welding booths	4 days	Tue 5/26/26	Fri 5/29/26	19	NA	NA
21			Plumbing welding gas	3 days	Tue 5/26/26	Thu 5/28/26	8	NA	NA
22			Install masonry frames	3 days	Tue 6/2/26	Thu 6/4/26	17	NA	NA

Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




















ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Actual Start	Actual Finish
23			Door frames, Doors & Hardware	3 days	Mon 5/4/26	Wed 5/6/26		NA	NA
24			Hang drywall (concession 182)	1 day	Tue 5/26/26	Tue 5/26/26	19	NA	NA
25			Finish drywall	3 days	Wed 5/27/26	Fri 5/29/26	24	NA	NA
26			Structural steel at RTU	1 day	Tue 6/2/26	Tue 6/2/26	13	NA	NA
27			Duct installation	5 days	Wed 6/3/26	Tue 6/9/26	26	NA	NA
28			Set RTU's	1 day	Wed 6/3/26	Wed 6/3/26	26	NA	NA
29			1st Coat Paint	2 days	Wed 6/10/26	Thu 6/11/26	27	NA	NA
30			Install wall accessories	1 day	Fri 6/12/26	Fri 6/12/26	29	NA	NA
31			ABOVE CEILING INSPECTION	1 day	Wed 6/10/26	Wed 6/10/26	27	NA	NA
32			ACP Ceilings (172S, 182, patch 173)	1 day	Fri 6/12/26	Fri 6/12/26	29	NA	NA
33			Install lockers	2 days	Fri 6/12/26	Mon 6/15/26	29	NA	NA
34			Install LVT (172S,173)	3 days	Fri 6/12/26	Tue 6/16/26	29	NA	NA
35			Final Paint	3 days	Wed 6/17/26	Fri 6/19/26	34	NA	NA
36			Final Clean	3 days	Mon 6/22/26	Wed 6/24/26	35	NA	NA
37			PUNCH LIST	1 day	Thu 6/25/26	Thu 6/25/26	36	NA	NA
38			Girls Locker room	44 days	Wed 5/20/26	Mon 7/20/26		NA	NA
39			MEP Demo	2 days	Wed 5/20/26	Thu 5/21/26	5,2	NA	NA
40			Cederburg Demo	5 days	Thu 5/21/26	Wed 5/27/26	6	NA	NA
41			Underground rough in.	3 days	Fri 5/29/26	Tue 6/2/26	40	NA	NA
42			Slab pour	2 days	Wed 6/3/26	Thu 6/4/26	41	NA	NA
43			CMU Walls	5 days	Tue 6/2/26	Mon 6/8/26	17,40	NA	NA

Project: 3.4.26 Summer Schedule
Date: Wed 3/4/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Actual Start	Actual Finish
44			Locker base pour	2 days	Tue 6/9/26	Wed 6/10/26	43	NA	NA
45			MEP ceiling rough in	2 days	Fri 6/5/26	Mon 6/8/26	42	NA	NA
46			ABOVE CEILING INSPECT	1 day	Tue 6/9/26	Tue 6/9/26	45	NA	NA
47			Tile shower room	2 days	Tue 6/9/26	Wed 6/10/26	43	NA	NA
48			Metal Framing - Ceiling	3 days	Thu 6/11/26	Tue 6/16/26	43,47	NA	NA
49			Hang drywall - ceiling	2 days	Wed 6/17/26	Thu 6/18/26	48	NA	NA
50			Finish drywall ceiling	4 days	Fri 6/19/26	Wed 6/24/26	49	NA	NA
51			Door frames, doors & hardware	3 days	Tue 6/9/26	Thu 6/11/26	43	NA	NA
52			1st Coat Paint	3 days	Thu 6/25/26	Mon 6/29/26	50	NA	NA
53			MEP Ceiling Devices	5 days	Tue 6/30/26	Mon 7/6/26	52	NA	NA
54			Locker install	3 days	Tue 6/30/26	Thu 7/2/26	52	NA	NA
55			Flooring Install - HPC	5 days	Tue 6/30/26	Fri 7/10/26	52	NA	NA
56			Doors & Hardware	3 days	Tue 7/14/26	Thu 7/16/26	55	NA	NA
57			Final paint	3 days	Mon 7/13/26	Wed 7/15/26	55	NA	NA
58			MEP device out	2 days	Fri 7/17/26	Mon 7/20/26	57	NA	NA
59			Specialties Install	2 days	Mon 7/13/26	Tue 7/14/26	55	NA	NA
60			Final Clean	1 day	Thu 7/16/26	Thu 7/16/26	59	NA	NA
61			PUNCH LIST	1 day	Mon 7/20/26	Mon 7/20/26	60	NA	NA
62			High School main entrance	71 days?	Mon 5/4/26	Mon 8/10/26		NA	NA
63			Temp walls and floor protection	3 days	Wed 5/20/26	Fri 5/22/26	2	NA	NA
64			MEP Demo	3 days	Fri 5/22/26	Tue 5/26/26	39	NA	NA
65			Cederburg Demo	4 days	Thu 5/28/26	Tue 6/2/26	40	NA	NA

























Project: 3.4.26 Summer Schedule
Date: Wed 3/4/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Actual Start	Actual Finish
66			Cut in and place ember	2 days	Tue 6/9/26	Wed 6/10/26	43,65	NA	NA
67			Footings - (CF-1, CF-4)	2 days	Wed 6/3/26	Thu 6/4/26	65	NA	NA
68			Form and pour cast-in-place wall	2 days	Fri 6/5/26	Mon 6/8/26	67	NA	NA
69			MEP ground rough	3 days	Wed 6/3/26	Fri 6/5/26	65	NA	NA
70			Floor pour	2 days	Mon 6/8/26	Tue 6/9/26	69	NA	NA
71			CMU walls and repair	3 days	Thu 6/11/26	Mon 6/15/26	66,70	NA	NA
72			MEP Ceiling rough in	4 days	Tue 6/16/26	Fri 6/19/26	71	NA	NA
73			ABOVE CEILING INSPECTION	1 day	Mon 6/22/26	Mon 6/22/26	72	NA	NA
74			Hollow metal door frame	3 days	Tue 6/16/26	Thu 6/18/26	71	NA	NA
75			Steel erection	2 days	Tue 6/9/26	Wed 6/10/26	68	NA	NA
76			parapet and soffit frame	2 days	Thu 6/11/26	Fri 6/12/26	75	NA	NA
77			Install can lighting in soffit	1 day	Mon 6/15/26	Mon 6/15/26	76	NA	NA
78			Parapet Carpentry	3 days	Mon 6/15/26	Wed 6/17/26	76	NA	NA
79			Install EIFS	3 days	Thu 6/18/26	Mon 6/22/26	78	NA	NA
80			spray foam insulation in parapet	1 day	Mon 6/15/26	Mon 6/15/26	76	NA	NA
81			Roof install	2 days	Tue 6/16/26	Wed 6/17/26	80	NA	NA
82			Aluminum glazing	2 days	Wed 6/10/26	Thu 6/11/26	70	NA	NA
83			Wall framing	3 days	Wed 6/10/26	Mon 6/22/26	70	NA	NA
84			Hang drywall	2 days	Fri 6/26/26	Mon 6/29/26	83	NA	NA
85			Finish drywall	4 days	Wed 7/8/26	Wed 7/15/26	84	NA	NA
86			1st coat paint	2 days	Mon 7/20/26	Tue 7/21/26	85	NA	NA
87			GWB ceiling framing	1 day?	Mon 5/4/26	Mon 5/4/26		NA	NA
















Project: 3.4.26 Summer Schedule
Date: Wed 3/4/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Actual Start	Actual Finish
88			Flooring	5 days	Tue 7/28/26	Mon 8/3/26	86	NA	NA
89			Casework	2 days	Wed 7/22/26	Thu 7/23/26	86	NA	NA
90			Doors and hardware	3 days	Tue 8/4/26	Thu 8/6/26	88	NA	NA
91			Final paint	3 days	Fri 7/24/26	Mon 8/3/26	89	NA	NA
92			Final Clean	3 days	Tue 8/4/26	Fri 8/7/26	91	NA	NA
93			PUNCH LIST	1 day	Mon 8/10/26	Mon 8/10/26	92	NA	NA
94			Elementary entrance	56 days	Wed 5/27/26	Wed 8/12/26		NA	NA
95			MEP Demo	2 days	Wed 5/27/26	Thu 5/28/26	64,2	NA	NA
96			Cederburg Demo	2 days	Wed 6/3/26	Thu 6/4/26	65	NA	NA
97			Wall framing (interior)	3 days	Fri 6/5/26	Tue 6/9/26	96	NA	NA
98			footings	2 days	Fri 6/5/26	Mon 6/8/26	96	NA	NA
99			Structural steel	3 days	Thu 6/11/26	Mon 6/15/26	75,98	NA	NA
100			pour stoops	1 day	Tue 6/16/26	Tue 6/16/26	99	NA	NA
101			Pour sidewalk	1 day	Wed 6/17/26	Wed 6/17/26	100	NA	NA
102			Roof/soffit framing (ex	3 days	Tue 6/16/26	Thu 6/18/26	99	NA	NA
103			MEP wall/ceiling rough	3 days	Wed 6/10/26	Fri 6/12/26	97	NA	NA
104			ABOVE CEILING INSPEC	1 day	Mon 6/15/26	Mon 6/15/26	103	NA	NA
105			Drywall hang	1 day	Mon 6/15/26	Mon 6/15/26	103	NA	NA
106			Drywall finish	4 days	Tue 6/16/26	Thu 6/25/26	105	NA	NA
107			1st coat paint	2 days	Tue 6/30/26	Wed 7/1/26	106	NA	NA
108			ACP ceilings	3 days	Thu 7/2/26	Mon 7/6/26	107	NA	NA
109			Flooring	3 days	Wed 7/8/26	Mon 7/13/26	108	NA	NA
110			Doors and hardware	2 days	Fri 7/17/26	Mon 7/20/26	109	NA	NA

Project: 3.4.26 Summer Schedu
Date: Wed 3/4/26




















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Actual Start	Actual Finish
111			Final paint	2 days	Wed 8/5/26	Thu 8/6/26	91,109	NA	NA
112			MEP device out	2 days	Mon 7/13/26	Tue 7/14/26	108	NA	NA
113			Final clean	2 days	Mon 8/10/26	Tue 8/11/26	111	NA	NA
114			PUNCH LIST	1 day	Wed 8/12/26	Wed 8/12/26	113	NA	NA
115			Corridor	54 days	Fri 6/5/26	Wed 8/19/26		NA	NA
116			MEP Demo	5 days	Fri 6/5/26	Thu 6/11/26	96,2	NA	NA
117			Cederburg demo	2 days	Fri 6/12/26	Mon 6/15/26	116	NA	NA
118			Frame 2hr wall in corridor 178	1 day	Fri 6/19/26	Fri 6/19/26	117	NA	NA
119			MEP wall rough in corridor 178	2 days	Tue 6/16/26	Wed 6/17/26	117	NA	NA
120			MEP Ceiling rough	3 days	Mon 6/22/26	Wed 6/24/26	117	NA	NA
121			ABOVE CEILING INSPEC	1 day	Thu 6/25/26	Thu 6/25/26	120	NA	NA
122			ACP Ceiling grid	4 days	Tue 7/7/26	Fri 7/10/26	108,119	NA	NA
123			Ceiling devises, lights, diffusers.	3 days	Wed 7/15/26	Tue 7/21/26	122	NA	NA
124			ACP ceiling PAD OUT	2 days	Wed 7/22/26	Thu 7/23/26	123	NA	NA
125			Final Paint	3 days	Tue 8/11/26	Thu 8/13/26	111	NA	NA
126			Final Clean	3 days	Fri 8/14/26	Tue 8/18/26	125	NA	NA
127			PUNCH LIST	1 day	Wed 8/19/26	Wed 8/19/26	126	NA	NA
128			Wrestling room	25 days	Fri 6/12/26	Thu 7/16/26		NA	NA
129			MEP demo	1 day	Fri 6/12/26	Fri 6/12/26	116,2	NA	NA
130			Cederburg demo	2 days	Tue 6/16/26	Wed 6/17/26	129	NA	NA
131			Install columns and be	2 days	Thu 6/18/26	Fri 6/19/26	130	NA	NA

Project: 3.4.26 Summer Schedu
Date: Wed 3/4/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Actual Start	Actual Finish
132			Skim coat paneling	4 days	Mon 6/22/26	Thu 6/25/26	130,131	NA	NA
133			Install lockers	2 days	Fri 6/26/26	Mon 6/29/26	132	NA	NA
134			Paint/Final paint	2 days	Fri 6/26/26	Mon 6/29/26	132	NA	NA
135			Flooring (WCPT & WB)	1 day	Tue 7/7/26	Tue 7/7/26	134	NA	NA
136			Final Cleaning	2 days	Wed 7/8/26	Fri 7/10/26	36,135	NA	NA
137			PUNCH LIST	1 day	Thu 7/16/26	Thu 7/16/26	136	NA	NA
138			FIRE FINAL FOR SCHOOL	1 day	Fri 7/17/26	Fri 7/17/26	137	NA	NA
139			Substantial Completion	1 day	Mon 7/20/26	Mon 7/20/26	138	NA	NA

Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Resource Names	Total Slack	Free Slack	26							Mar 8, '26							Mar 15, '26							Mar 22, '26							Mar 29, '26		
			T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T		
J & H Specialties	24 days	0 days																															
Elite Storage Products	37 days	37 days																															
Kucera Painting Final	24 days	0 days																															
Work Space Flooring	24 days	0 days																															
Final Clean	24 days	0 days																															
OAC	22 days	0 days																															
	22 days	0 days																															
	22 days	22 days																															




Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

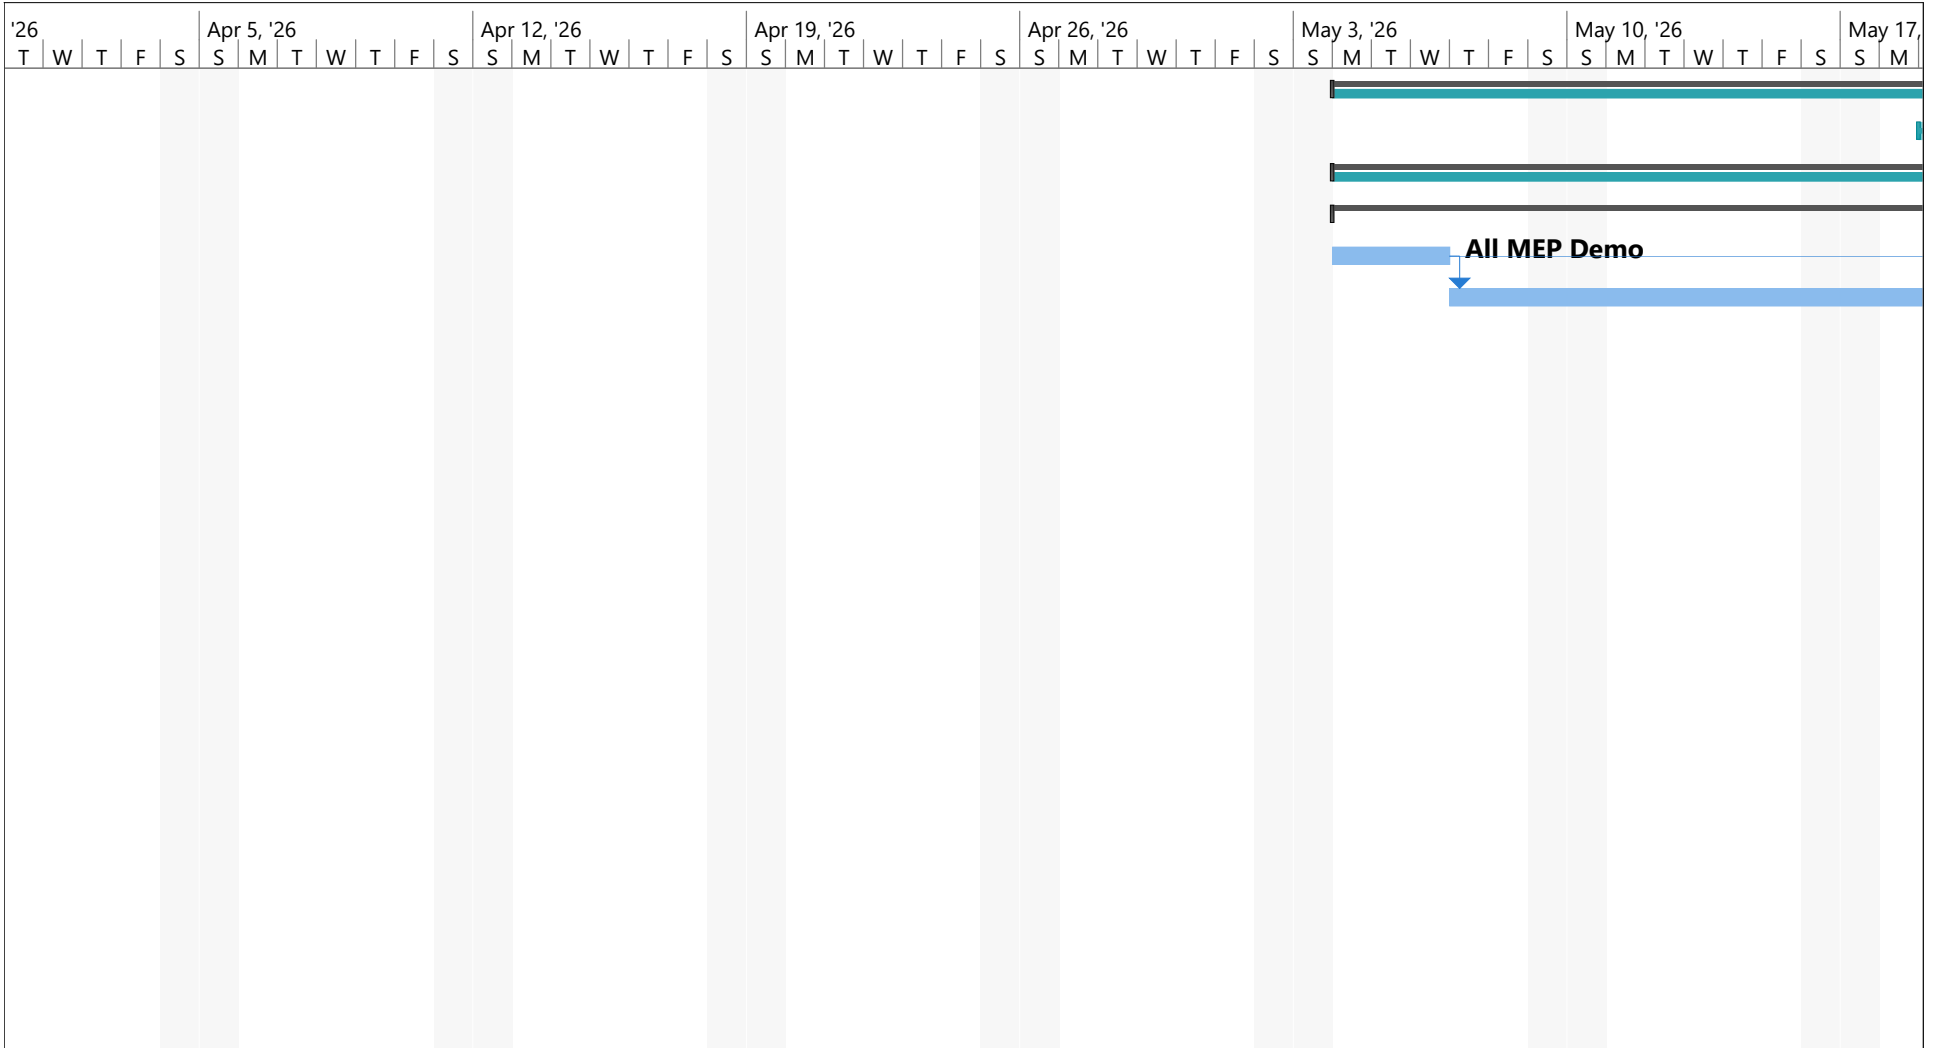


Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

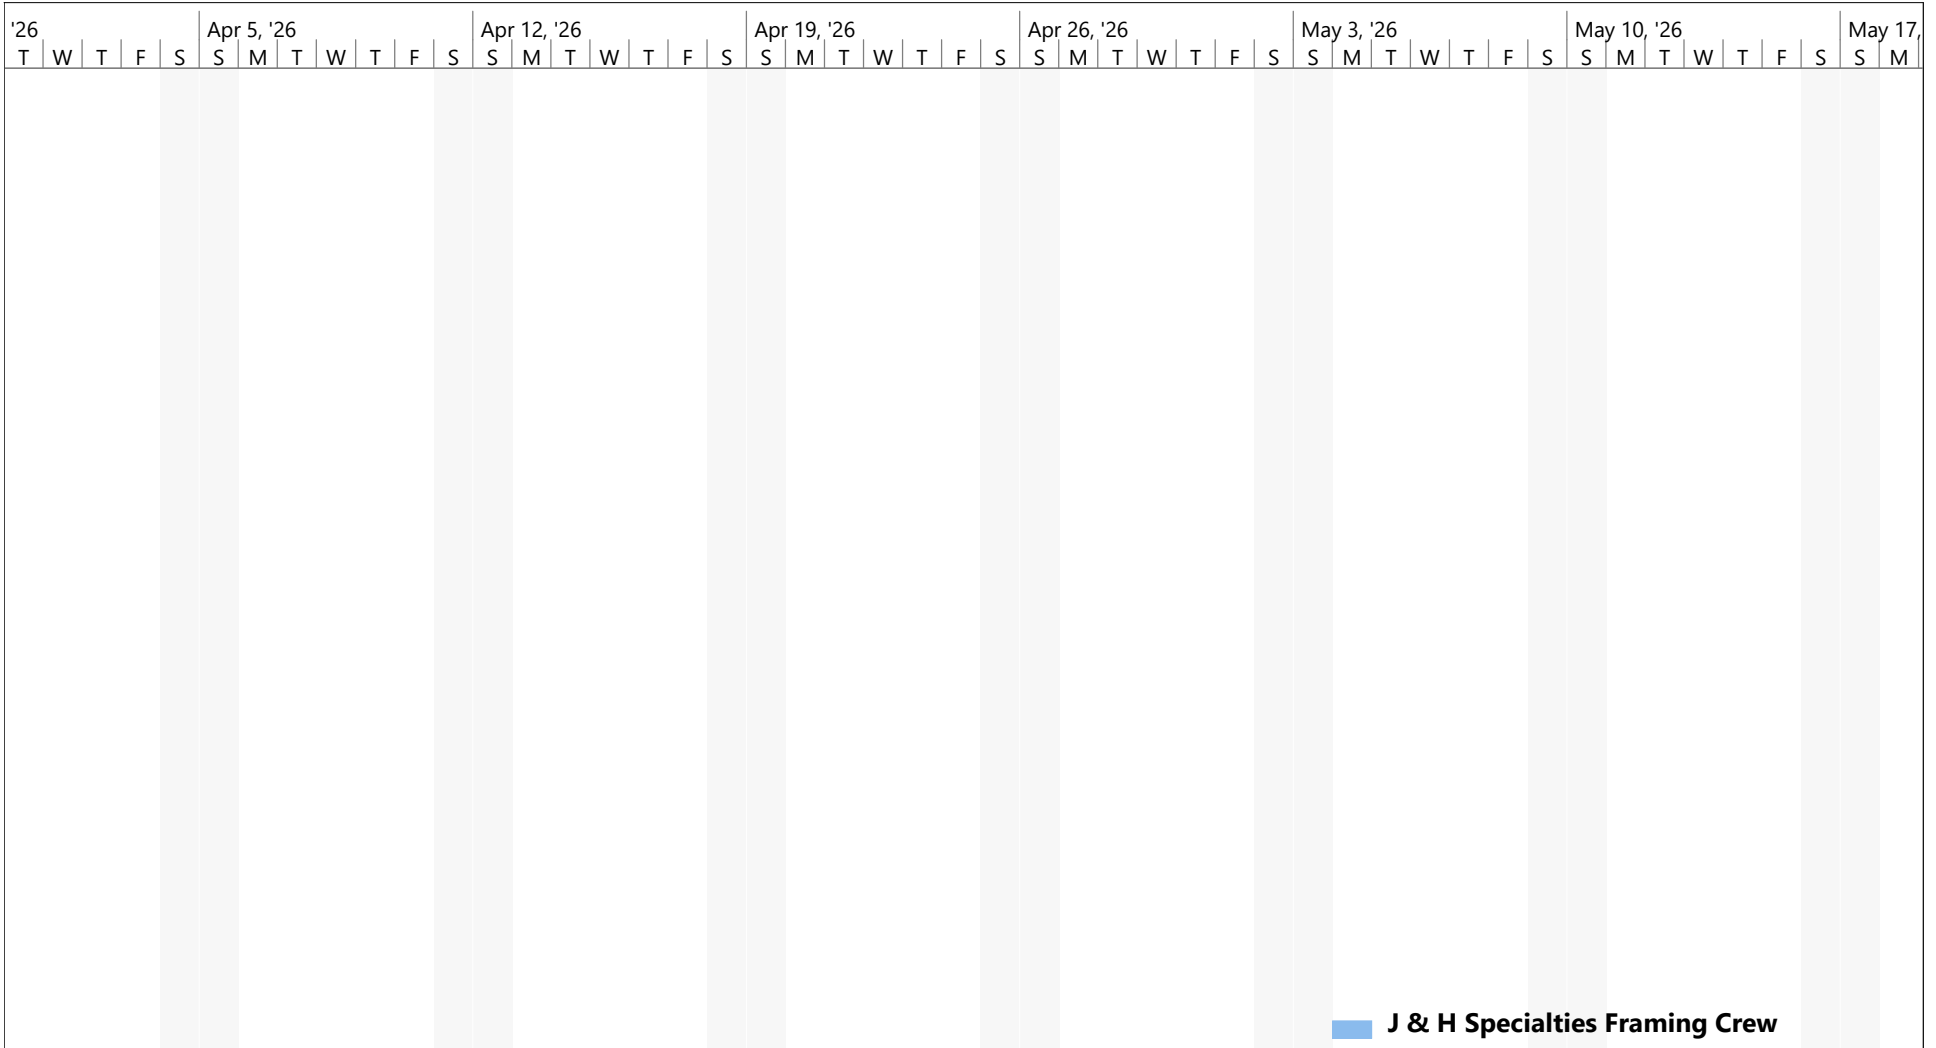


Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

'26 May 24, '26 May 31, '26 Jun 7, '26 Jun 14, '26 Jun 21, '26 Jun 28, '26 Jul 5, '26
T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M

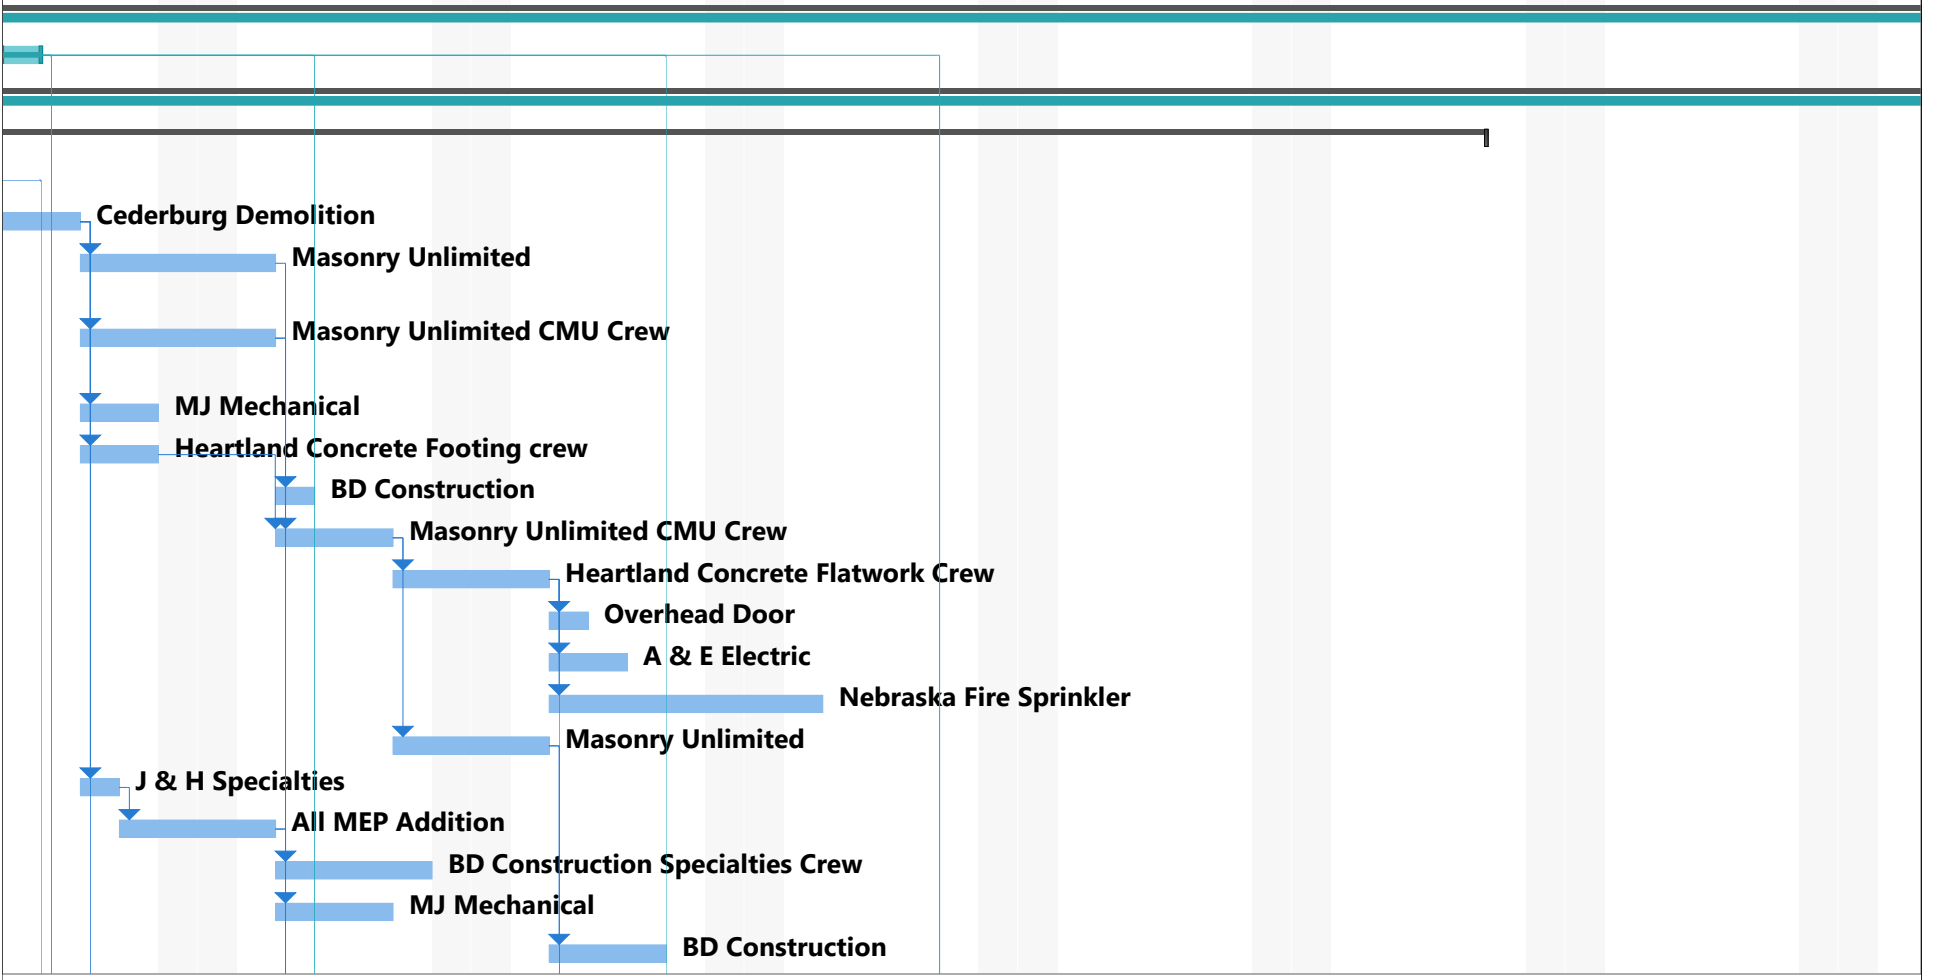


Project: 3.4.26 Summer Schedu
Date: Wed 3/4/26


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

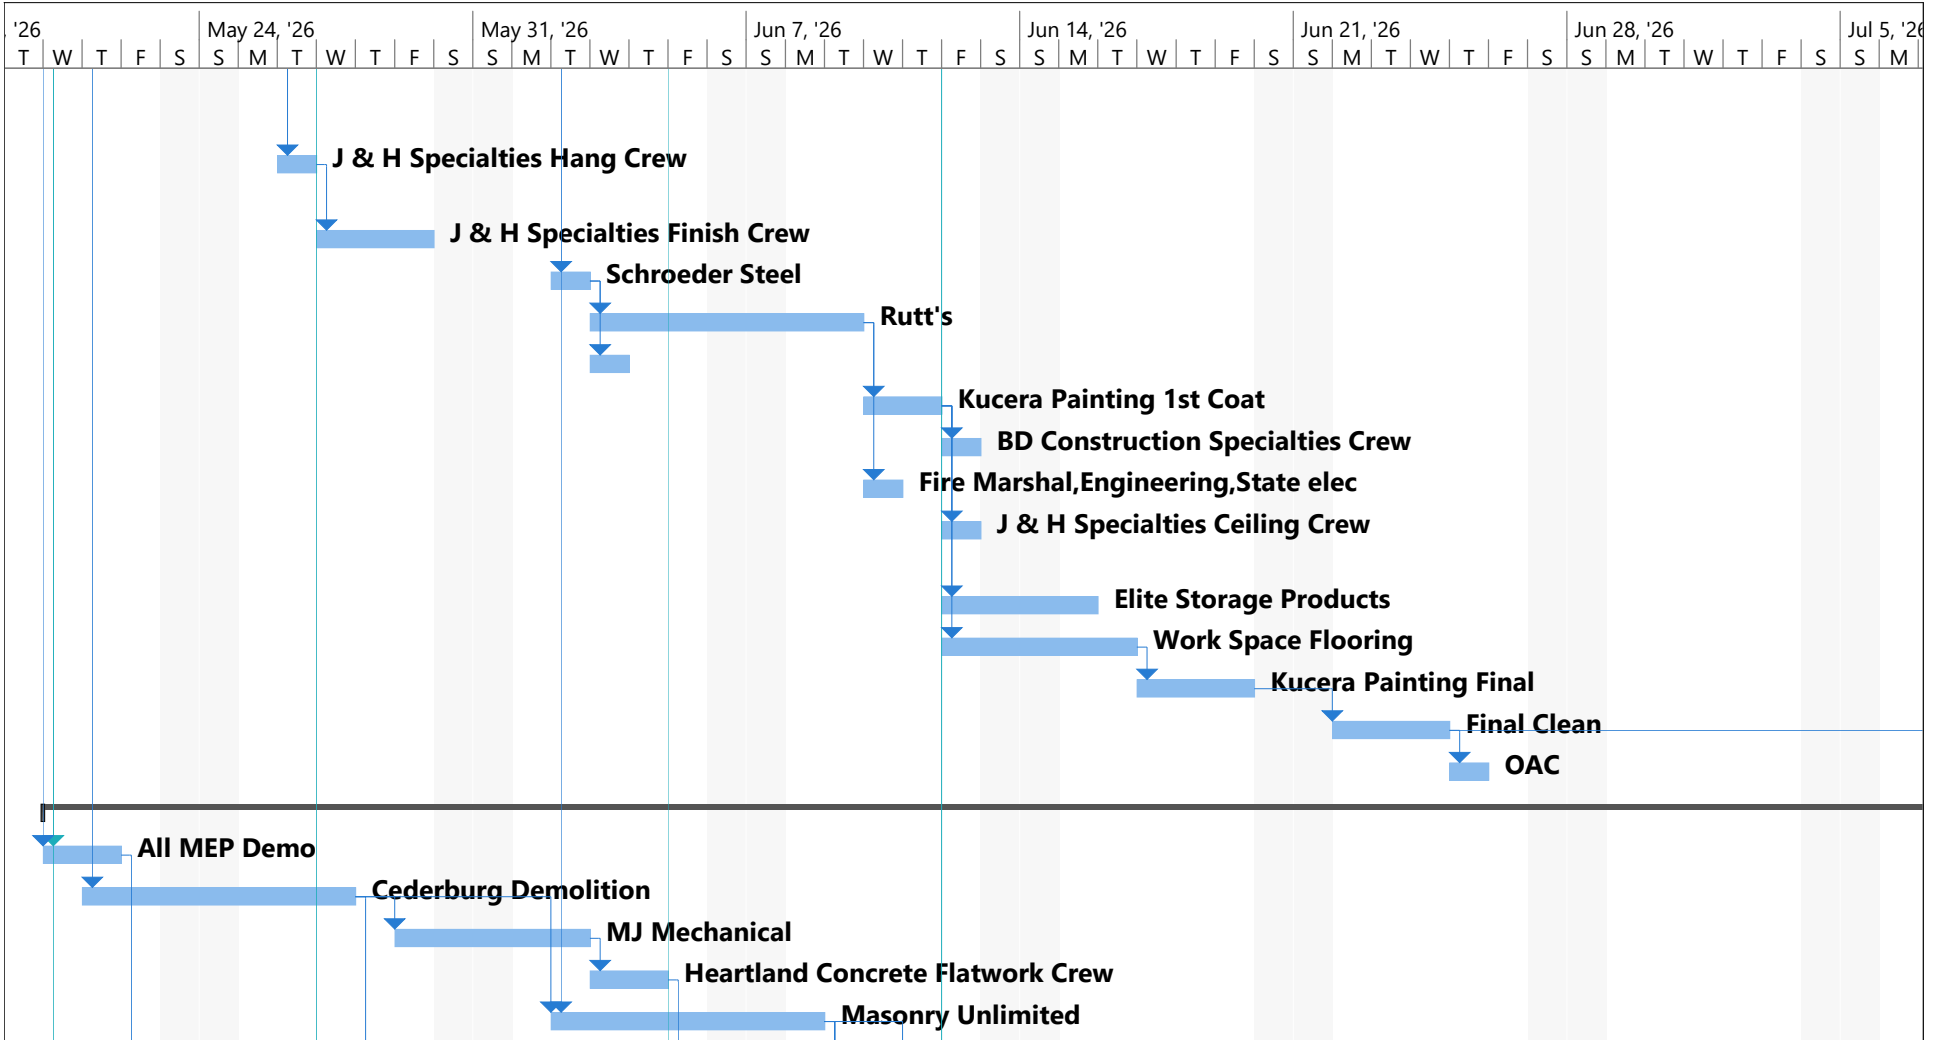


Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

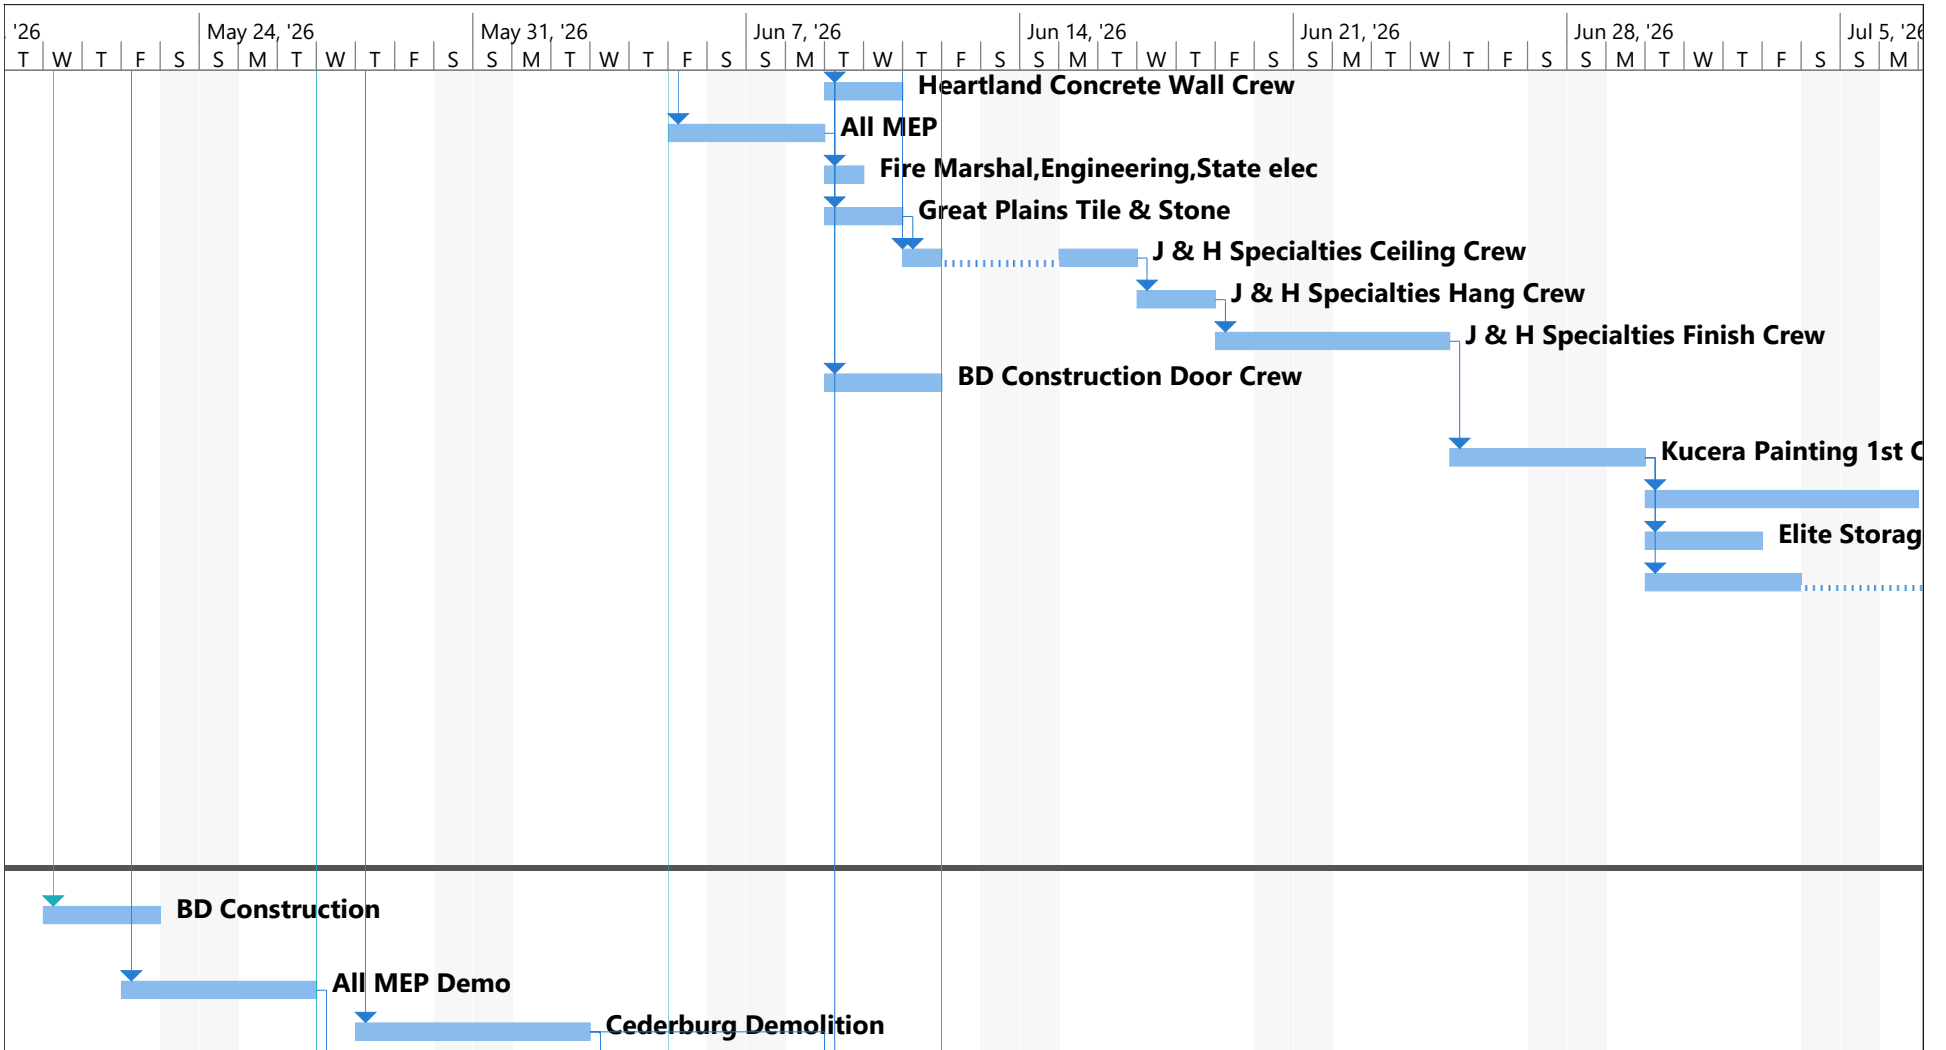


Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

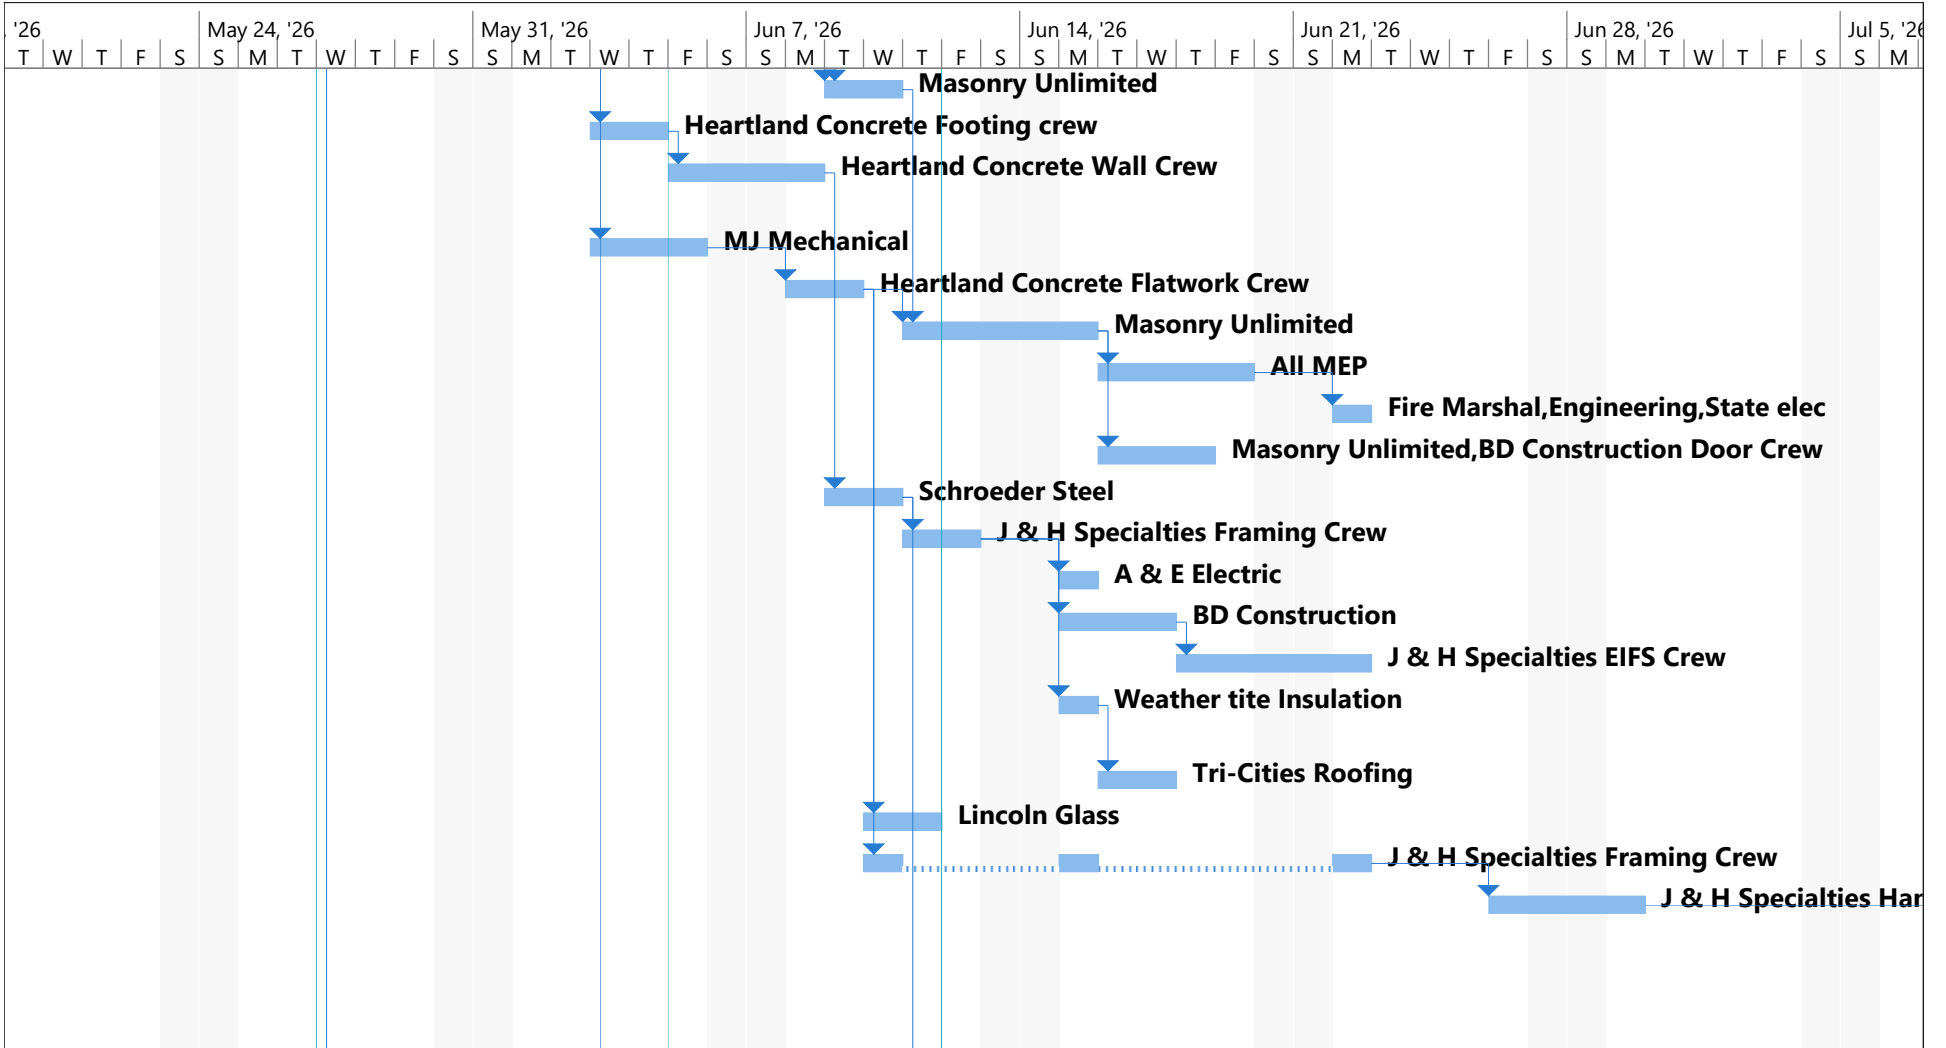

Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

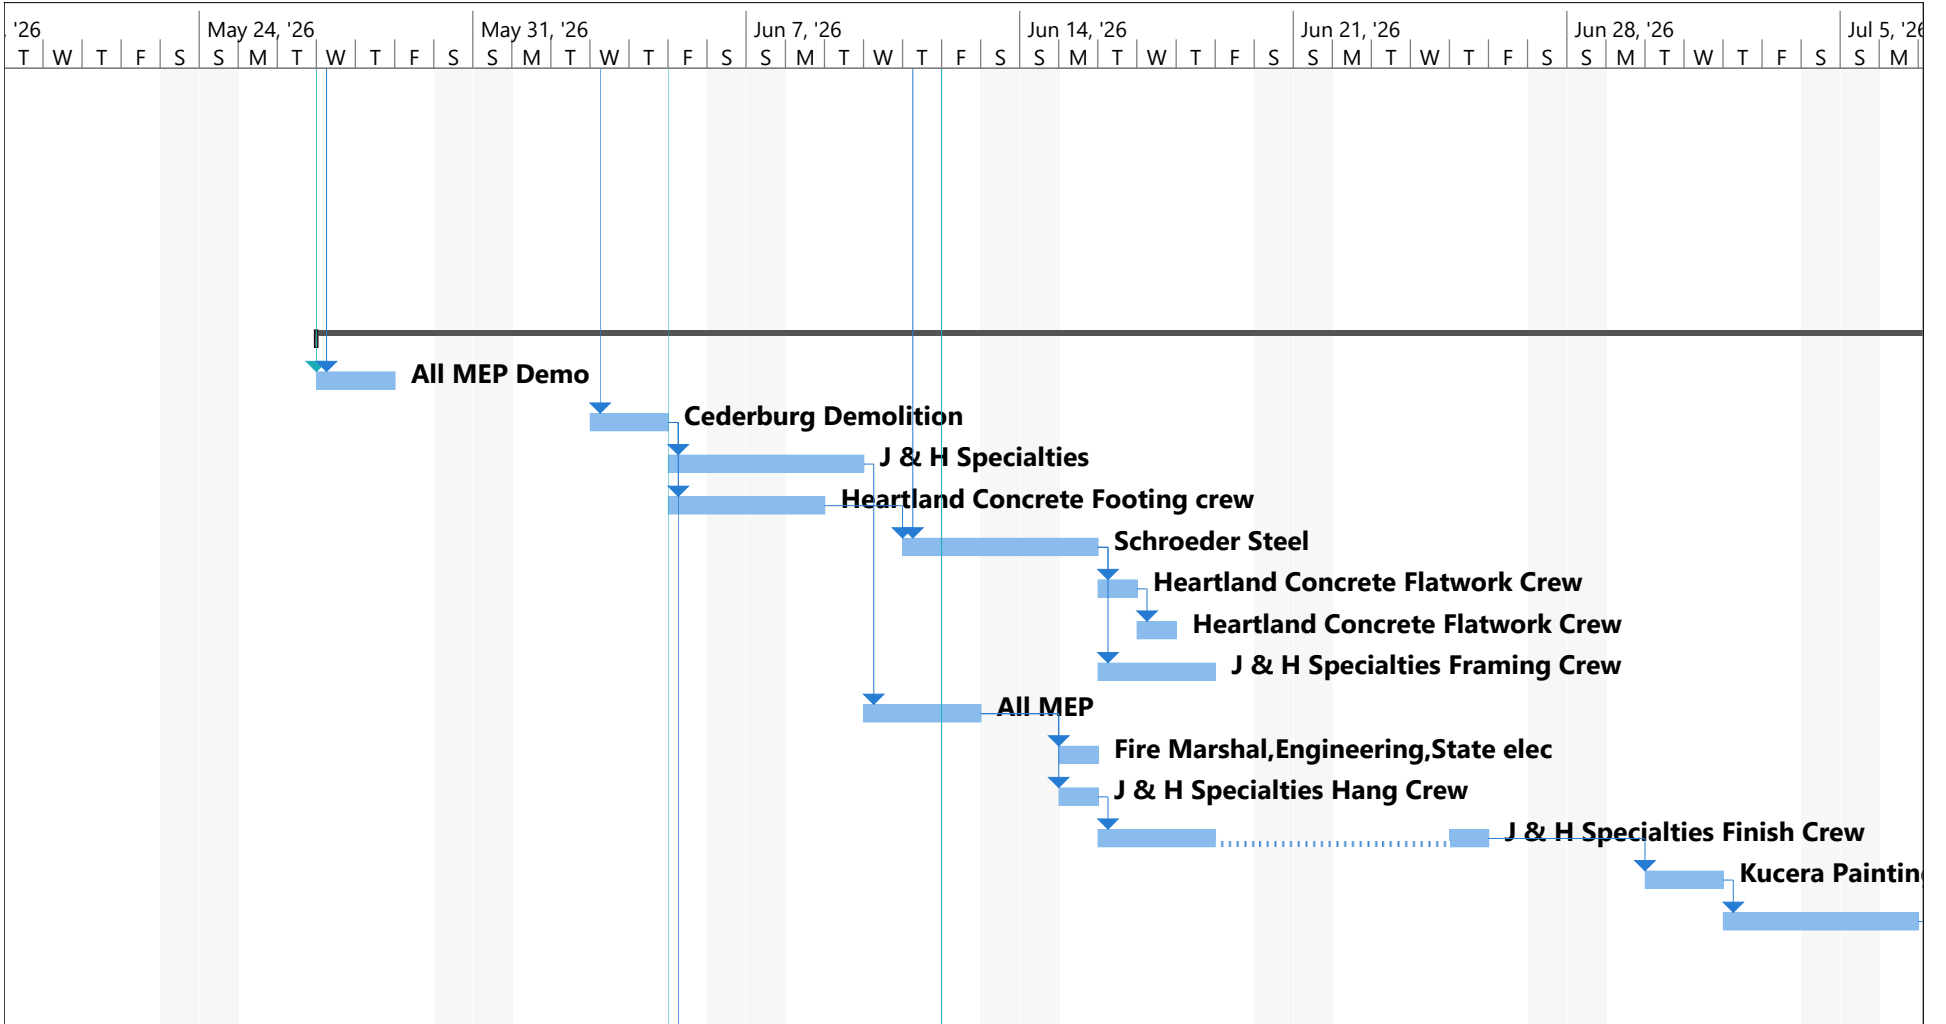


Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

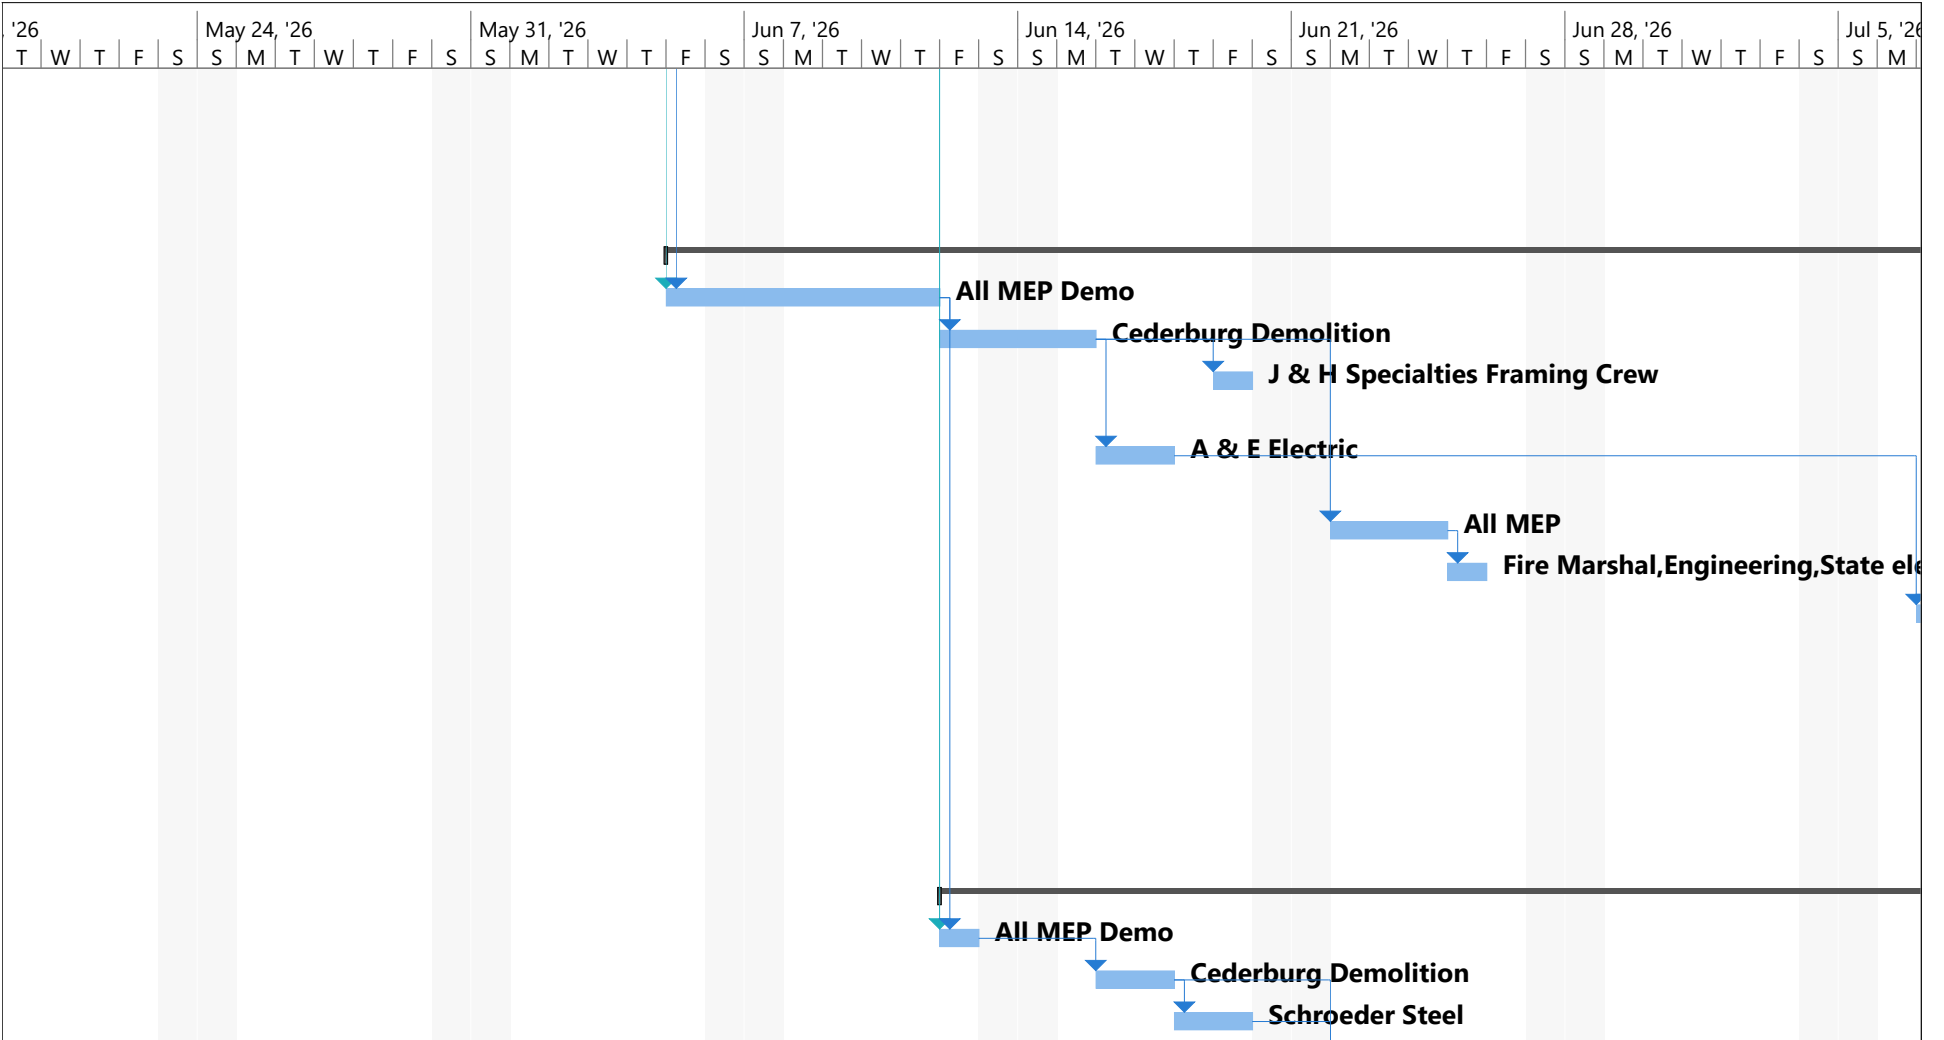


Project: 3.4.26 Summer Schedu
Date: Wed 3/4/26


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

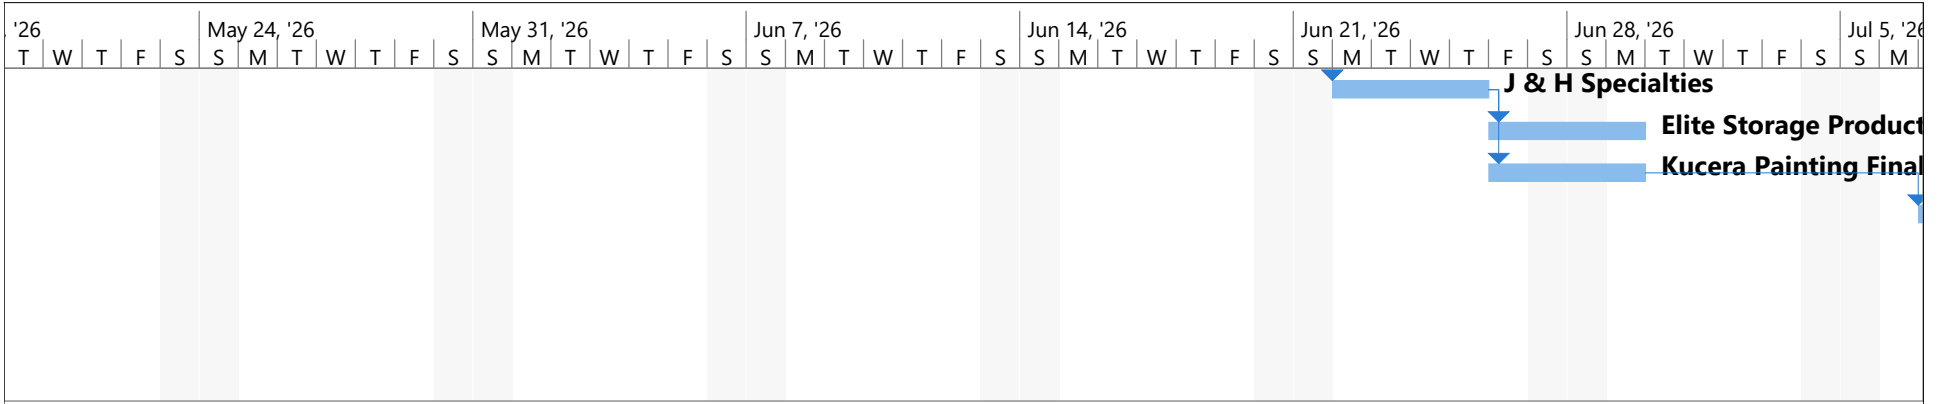


Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

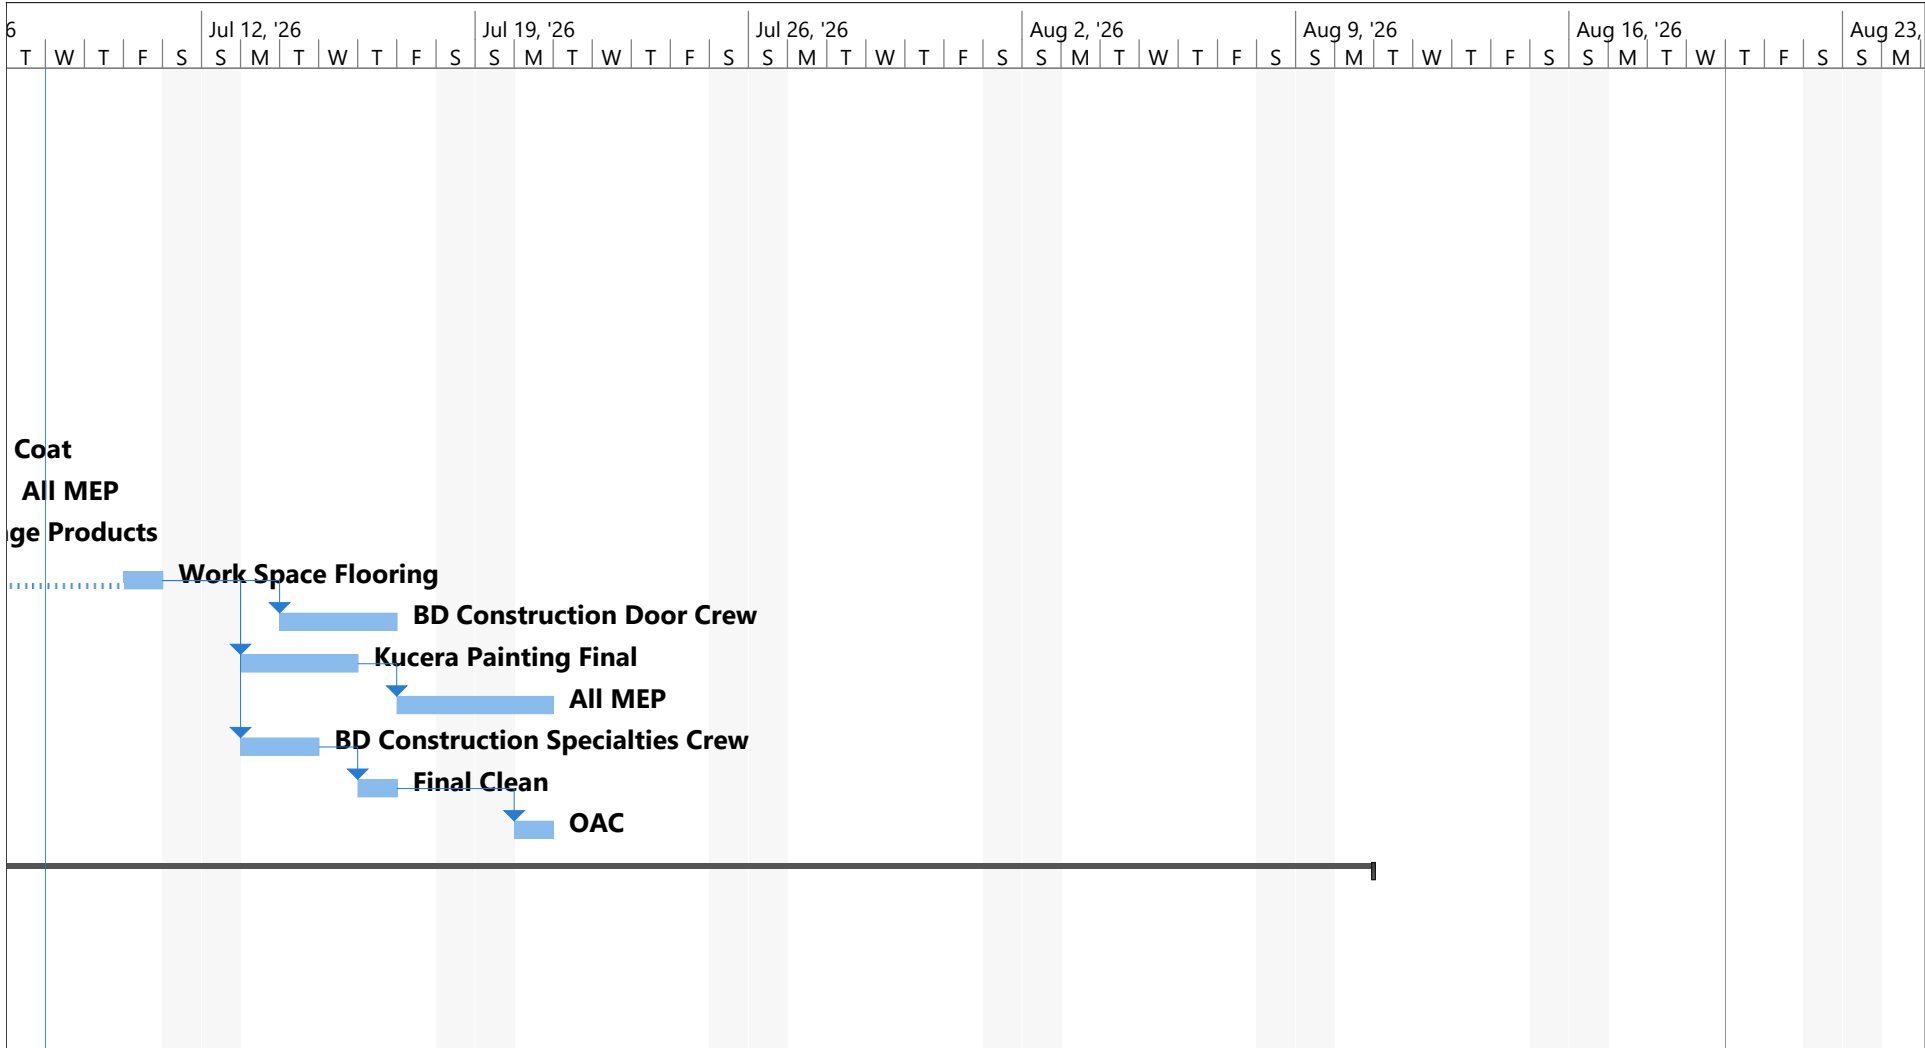


Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

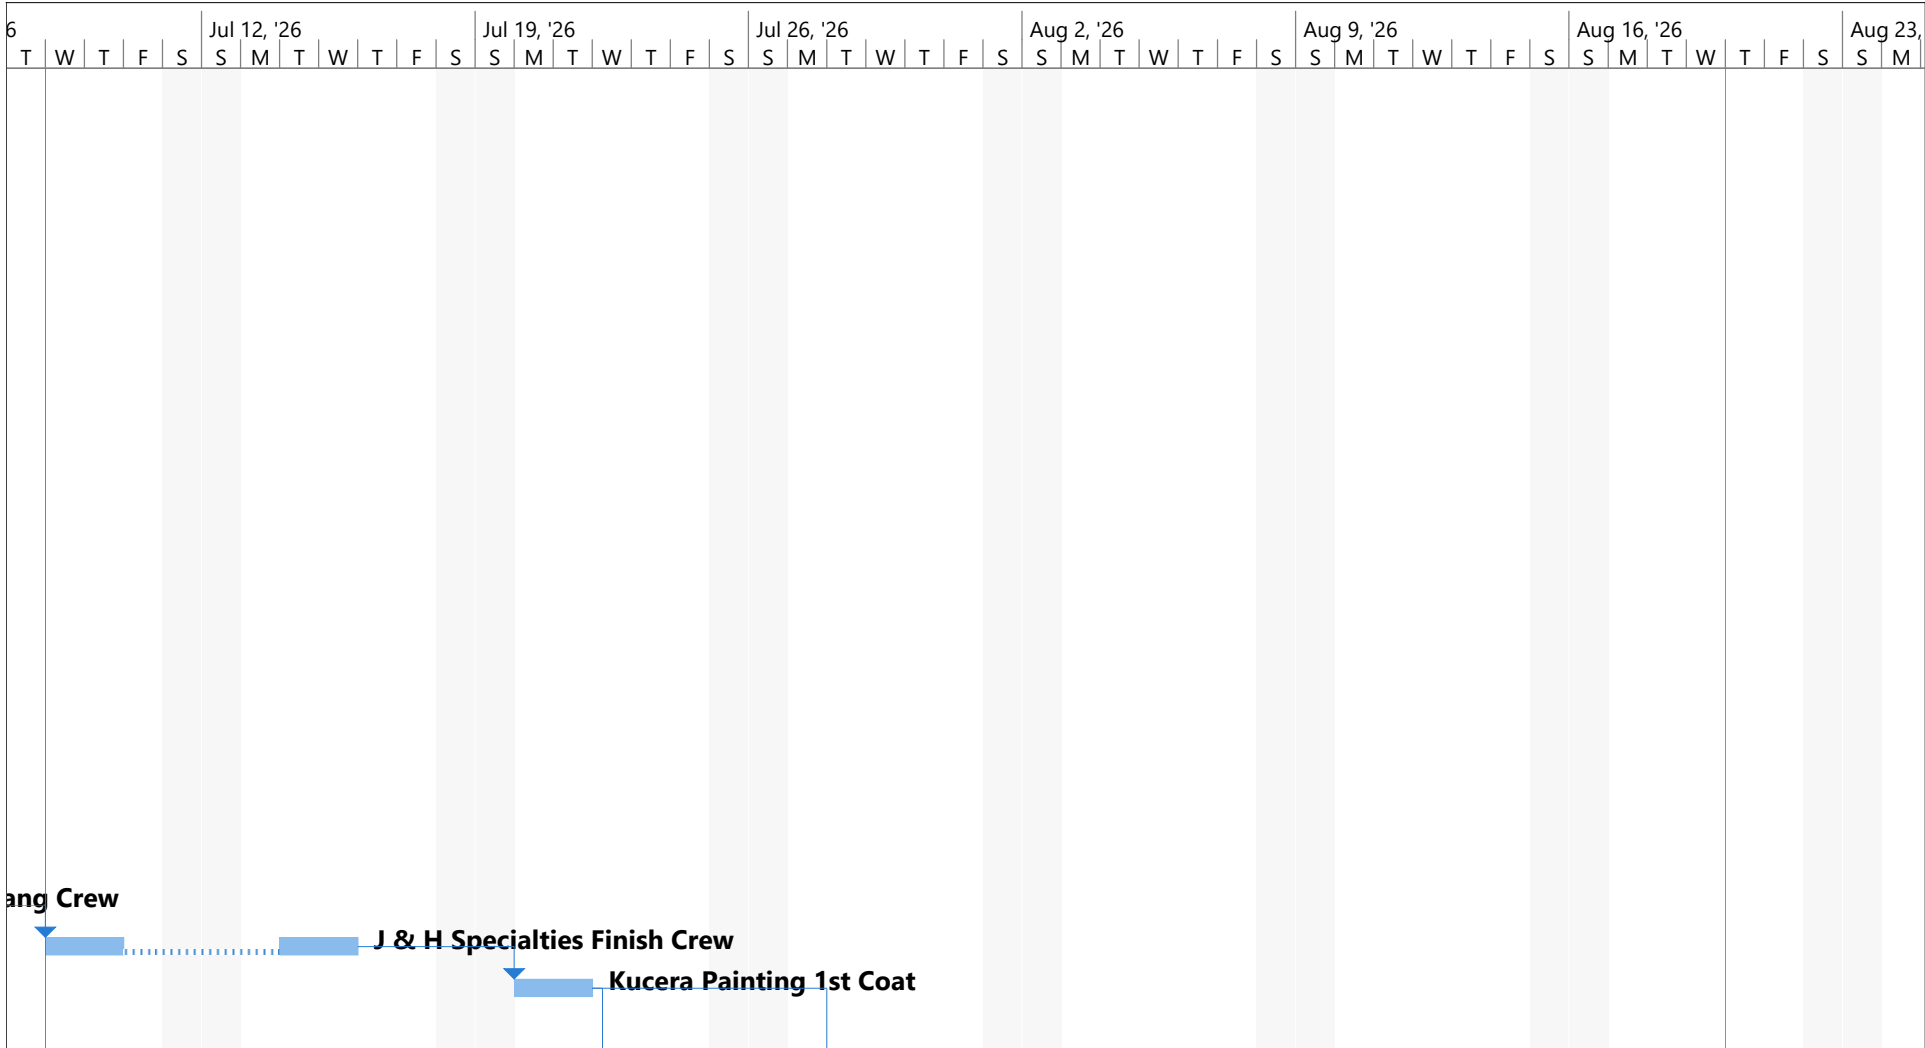


Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

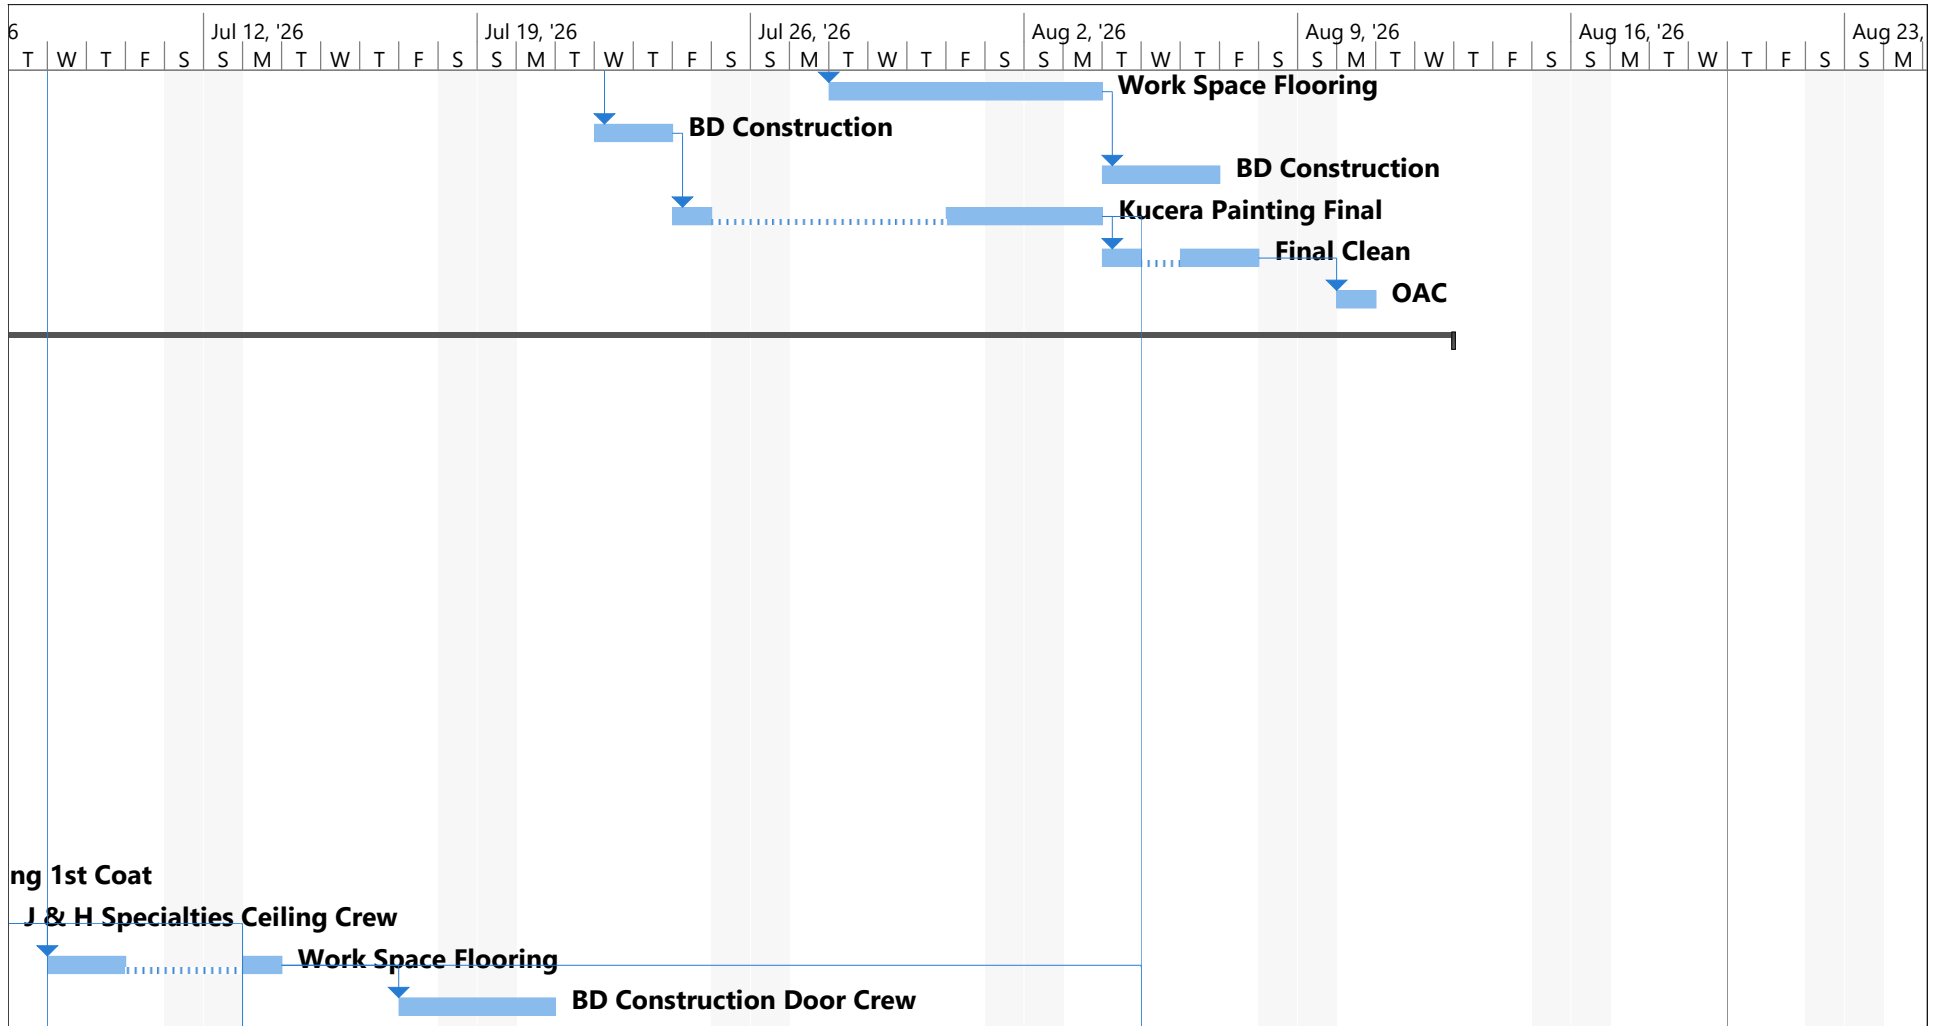

Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

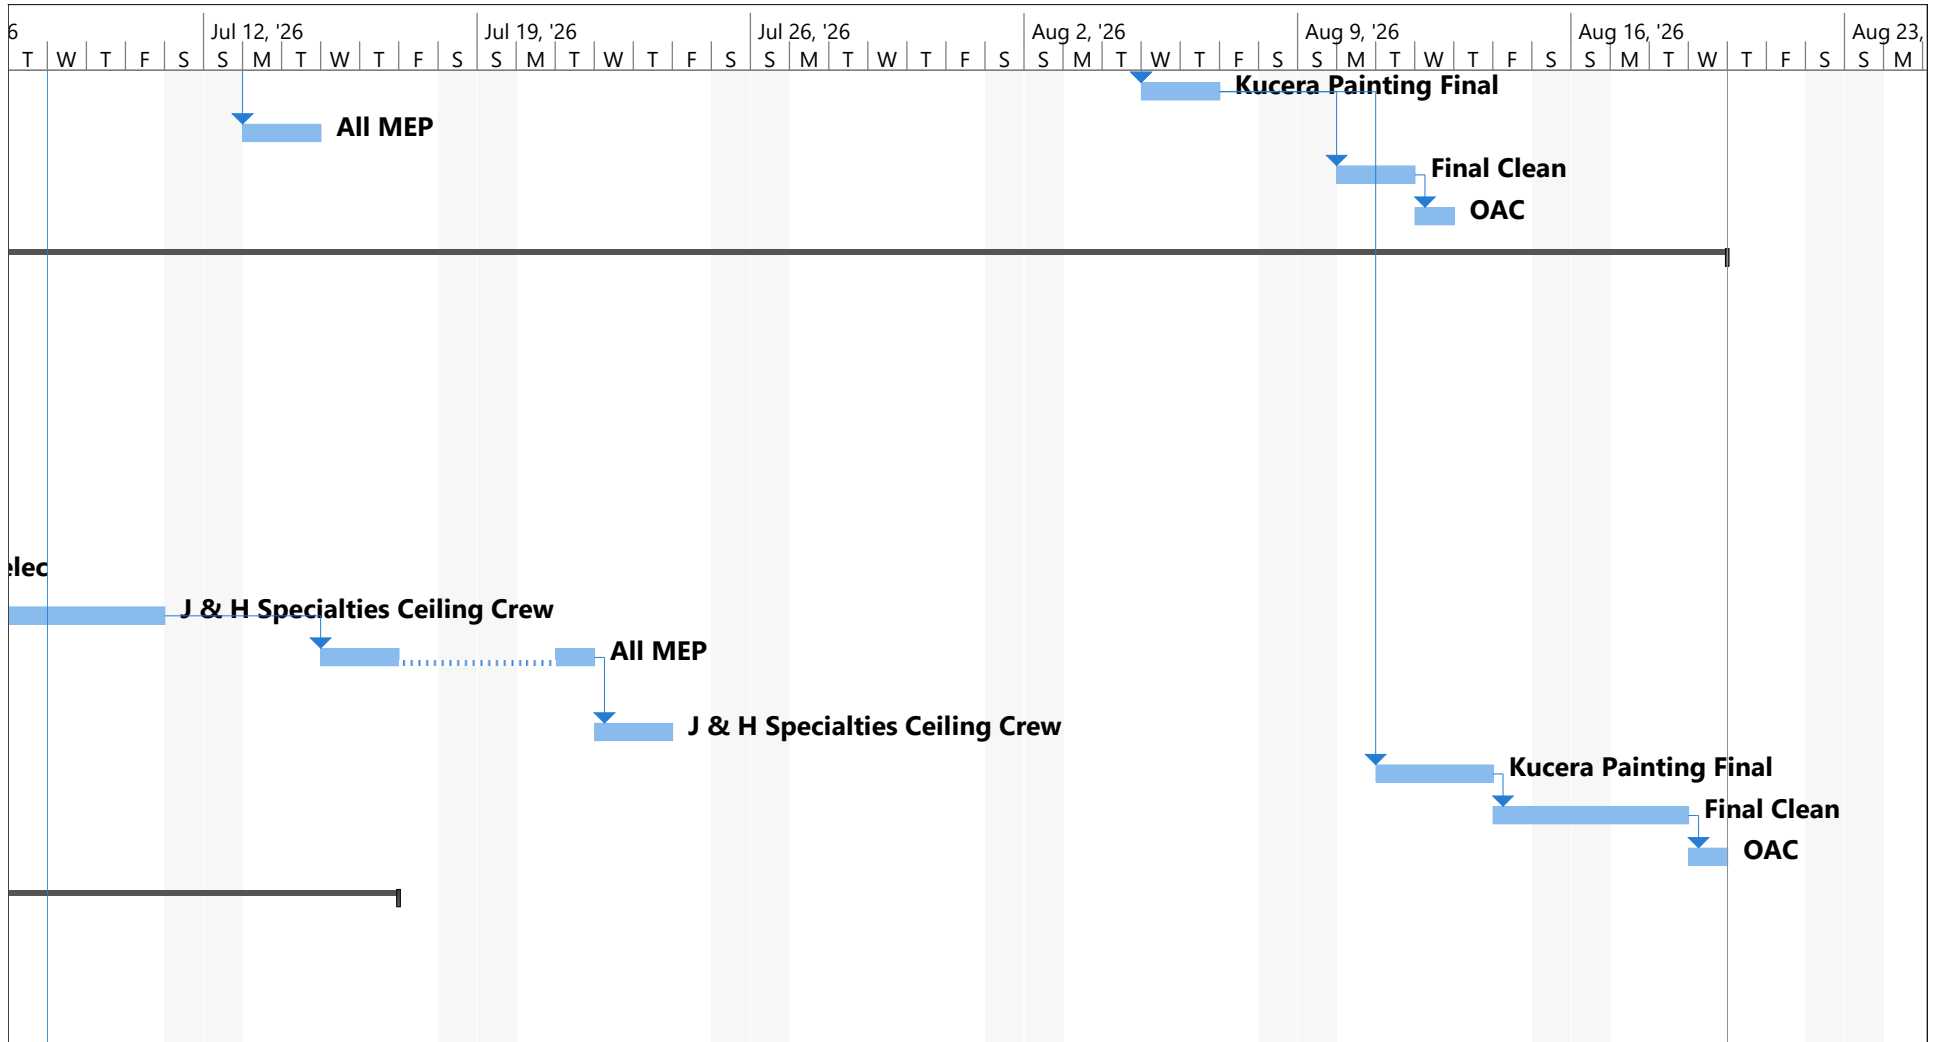

Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

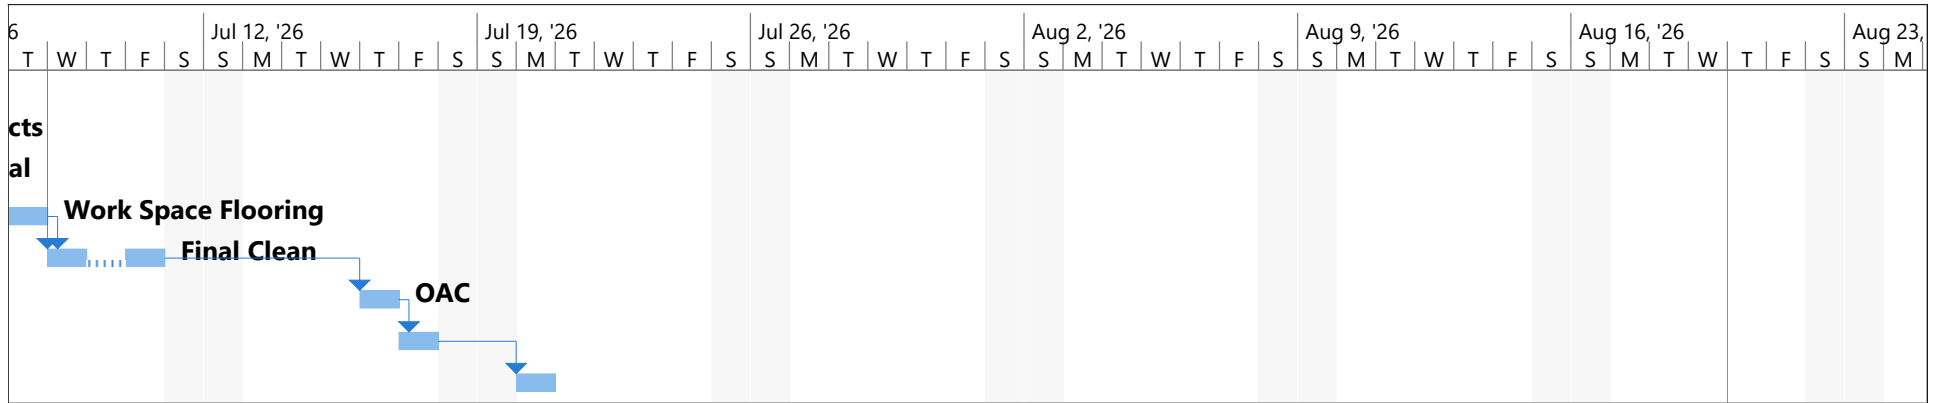

Project: 3.4.26 Summer Schedu Date: Wed 3/4/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
